

# CHANGE ORDER

## CONSTRUCTION MANAGER-ADVISER EDITION

Owner   
 Construction Manager   
 Architect   
 Contractor   
 Field   
 Other

PROJECT: **Loeb Stadium**  
 (Name and address) **Main Street and Wallace Street**  
**Lafayette, Indiana**

CHANGE ORDER NO.: **BP-1-5**  
 INITIATION DATE: **March 26, 2020**

TO CONTRACTOR: **J.R. Kelly Company, Inc.**  
 (Name and address) **3450 Concord Road**  
**Lafayette, IN 47909**

PROJECT NOS.: **6617**  
 CONTRACT FOR: **BP #1 - General Trades**  
 CONTRACT DATE: **June 4, 2019**

The Contract is changed as follows:

6617.036 - American Structurepoint Proposal Request #5, as it pertains to the press level drainage.	Add	\$443.00
6617.040 - American Structurepoint Proposal Request #7, as it pertains to field level drainage.	Add	\$5,471.00
6617.042 - American Structurepoint Proposal Request #8, as it pertains to door hardware changes	Deduct	-\$2,788.00
6617.045 - Foul pole foundation change as indicated in American Structurpoint response to RFI #70.	Add	\$987.00
	<b>TOTAL</b>	<b>\$4,113.00</b>

**Not valid until signed by the Owner, Construction Manager, Architect and Contractor.**

The original (Contract Sum) (Guaranteed Maximum Price) was.....	\$	10,480,000.00
Net change by previously authorized Change Orders.....	\$	37,695.00
The (Contract Sum) ( <del>Guaranteed Maximum Price</del> ) prior to this Change Order was.....	\$	10,517,695.00
The (Contract Sum) ( <del>Guaranteed Maximum Price</del> ) will be (increased) ( <del>decreased</del> ) ( <del>unchanged</del> ) by this Change Order.....	\$	4,113.00
The new (Contract Sum) ( <del>Guaranteed Maximum Price</del> ) including this Change Order will be.....	\$	10,521,808.00
The Contract Time will be ( <del>increased</del> ) ( <del>decreased</del> ) (unchanged) by .....	( 0 )	days
The dated of Substantial Completion as of the date of this Change Order therefore is .....		Unchanged

NOTE: This summary does not reflect changes in the Contract Sum, Contract Time or Guaranteed Maximum Price which have been authorized by Construction Change Directive.

Kettelhut Construction, Inc.  
 CONSTRUCTION MANAGER

740 Sagamore Parkway S., Lafayette, IN 47905  
 ADDRESS

 03/30/2020  
 BY DATE


J.R. Kelly Company, Inc.  
 CONTRACTOR

3450 Concord Road, Lafayette, IN 47909  
 ADDRESS

 3/30/20  
 BY DATE


American StructurePoint Inc.  
 ARCHITECT

157 East Maryland Street, Indianapolis, IN 46204  
 ADDRESS

 03.30.2020  
 BY DATE

City of Lafayette - Engineering  
 OWNER

20 N. 6th Street, Lafayette, IN 47901  
 ADDRESS

 4/15/2020  
 BY DATE

**740 Sagamore Parkway South  
Lafayette, IN 47905  
(765) 447-2181  
Fax (765) 447-7122**

January 22, 2020

Mr. Dan McCloskey  
American Structurepoint, Inc.  
9025 River Road, Suite 200  
Indianapolis, IN 46240

Re: Loeb Stadium Renovation  
Lafayette, Indiana  
Kettelhut Project No. 6617

Gentlemen:

Enclosed please find cost documentation from applicable Contractors regarding American Structurepoint Proposal Request No. 6, as it pertains to adding storm pipe and deck drains. We have yet to receive responses from Contractors labeled N/R, but do not anticipate any other costs or credits than those shown below.

1. BP #1 – General Trades	JR Kelly Co., Inc.	\$ 443.00
2. BP #2 – Masonry	James Scharer Masonry, Inc.	N/R
3. BP #3 – Steel	Almet, Inc.	N/R
4. BP #4 – Roofing	Horning Roofing & Sheet Metal Co., LLC	N/R
5. BP #5 – Alum.	Central Indiana Glass & Glazing, Inc.	N/R
6. BP #6 – Fire Sprinklers	Dalmatian Fire, Division of Shambaugh & Son, L.P.	N/R
7. BP #7 – Mechanical	D. A. Dodd, LLC	\$ 20,067.00
8. BP #8 – Electrical	Huston Electric, Inc.	N/R
9. BP #9 – Sports Lighting	Custer Electric, Inc.	N/R
10. BP #10 – Scoreboard		
11. BP #11 – Turf	Sprinturf, Inc.	N/R
12. BP #12 – Stadium Seat	Irwin Seating Company	N/R
13. BP #13 – Food Service	C&T Design & Equipment Co.	N/R
		<u>\$ 20,510.00</u>

After your review, if this cost data is approved by your firm and the Owner, please advise in order for a Change Order to be initiated.

Sincerely,

KETTELHUT CONSTRUCTION, INC.

*[Handwritten Signature]*  
D. Alex Gonzalez  
Executive Vice President

DAG: jas

Enclosure

cc: Field Office  
City of Lafayette w/enclosure  
Field Order 6617.036





7260 Shadeland Station, Indianapolis, Indiana 46256  
TEL 317.547.5580 FAX 317.543.0270

www.structurepoint.com

---

## Proposal Request No. 006

Project Name: Loeb Stadium  
Project Number: 2015.02410  
Date: 11/16/2019

---

### OWNER:

City of Lafayette, Indiana – Board of Public Works and Safety  
20 North 6<sup>th</sup> Street  
Lafayette, IN 47901

### ARCHITECT / STRUCTURAL ENGINEER / CIVIL ENGINEER

American Structurepoint, Inc.  
9025 River Road, Suite 200  
Indianapolis, Indiana 46240  
317.547.5580

### MECHANICAL / PLUMBING / ELECTRICAL ENGINEER

Applied Engineering Services, Inc.  
5975 Castle Creek Parkway N Drive, Suite 300  
Indianapolis, IN 46250  
317.810.4141

---

This Proposal Request is for informational and pricing purposes only and shall not be interpreted as instruction to perform the proposed Work indicated herein. Contractor shall detail all costs associated with the Work, itemized at a minimum by labor, material, overhead and profit. Specify whether the change in Work is an ADD, DEDUCT or NO CHANGE to the contract. After receiving pricing, the Architect shall direct the Contractor regarding how to proceed. If, and only if, the Work outlined in this Proposal Request causes no change in Contract sum or time, the Contractor may then proceed with the Work listed herein, at which point, said Work shall become part of the Contract Documents and modify the original Contract Documents and all prior changes as applicable. Requirements of the original Contract Documents and previous changes remain in effect except as modified by this Proposal Request.

The extent of this Proposal Request is as follows:

### DOCUMENT MODIFICATIONS

#### DRAWINGS

- A. See clouded revisions on the attached drawings.
1. Drawing P300.B add storm pipe below MECH/ELEC room 119.
  2. Drawing P302.B add storm pipe serving Deck Drains where shown.
  3. Drawing P303.B add Deck Drains DD-2 where shown on the Press Level Concourse.
  4. Drawing P601 "Drainage Fixture Schedule" DD-2 drain has change to similar to a J R Smith 1610.

END OF PROPOSAL REQUEST.

  
**J.R. KELLY COMPANY**  
GENERAL CONTRACTORS

December 13, 2019

Kettelhut Construction Inc.  
740 Sagamore Parkway South  
Lafayette, IN 47905

Attn: Alex Gonzalez

Re: PR #006 Added Press Level Drains Proposal  
Loeb Stadium – General Trades

J.R. Kelly Company is pleased to provide pricing associated with the changes shown in PR #006. During our conversations we were told that D.A. Dodd will provide and set all piping and the drains themselves into the steel decking. D.A. Dodd will also seal the drains at the deck so keep concrete from leaking through around the pipe. Thus our only work would be to install tape on the drains to protect them while we are placing and finishing the concrete. Our pricing includes installing and removing protective tape and then cleaning any concrete from the drain grate as needed. We have been told that the drains will not be recessed much (if any at all). So our pricing assumes that we are only dishing the concrete for a 12" diameter area around the drain at most. The drawings indicate that we are adding (7) seven drains at the press level. The cost associated with this work is:

JR Kelly Material	\$0
JR Kelly Labor (1 mnhr each)	\$399
10% OH&P	\$40
Bond	\$4

**TOTAL LUMP COST FOR CHANGE ... \$443\***

\*Note that if D.A. Dodd installs and removes protective tape and we do not need to provide any dishing of the concrete at the drains then there will be no added cost for us on this PR.

Our proposal is valid for 30 days. Please issue a Change Order for this work if you would like for us to incorporate this change into our work. If you have any questions or need additional information please contact our office at your earliest convenience. Thank you for the opportunity to work with you on this project.

Sincerely,



Robert Mutzl P.E.  
Executive VP

(765) 772-3991      FAX (765) 772-3996  
3450 CONCORD ROAD      LAFAYETTE, IN 47909

60617.036

**740 Sagamore Parkway South  
Lafayette, IN 47905  
(765) 447-2181  
Fax (765) 447-7122**

March 4, 2020

Mr. Dan McCloskey  
American Structurepoint, Inc.  
9025 River Road, Suite 200  
Indianapolis, IN 46240

Re: Loeb Stadium Renovation  
Lafayette, Indiana  
Kettelhut Project No. 6617

Gentlemen:

Enclosed please find cost documentation from applicable Contractors regarding PR #007, as it pertains to field drainage changes. We have yet to receive responses from Contractors labeled N/R, but do not anticipate any other costs or credits than those shown below.

1. BP #1 – General Trades	JR Kelly Co., Inc.	\$ 5,471.00
2. BP #2 – Masonry	James Señarel Masonry, Inc.	N/R
3. BP #3 – Steel	Almet, Inc.	N/R
4. BP #4 – Roofing	Horning Roofing & Sheet Metal Co., LLC	N/R
5. BP #5 – Alum.	Central Indiana Glass & Glazing, Inc.	N/R
6. BP #6 – Fire Sprinklers	Dalmatian Fire, Division of Shambaugh & Son, L.P.	N/R
7. BP #7 – Mechanical	D. A. Dodd, LLC	\$ 308.00
8. BP #8 – Electrical	Huston Electric, Inc.	N/R
9. BP #9 – Sports Lighting	Custer Electric, Inc.	N/R
10. BP #10 – Scoreboard		
11. BP #11 – Turf	Sprinturf, Inc.	\$ 0.00
12. BP #12 – Stadium Seat	Irwin Seating Company	N/R
13. BP #13 – Food Service	C&T Design & Equipment Co.	N/R
		<u>\$ 5,779.00</u>

After your review, if this cost data is approved by your firm and the Owner, please advise in order for a Change Order to be initiated.

Sincerely,

KETTELHUT CONSTRUCTION, INC.

D. Alex Gonzalez  
Executive Vice President

DAG: jas

Enclosure

cc: Field Office  
City of Lafayette w/enclosure  
Field Order 6617.040





7260 Shadeland Station, Indianapolis, Indiana 46256  
TEL 317.547.5580 FAX 317.543.0270

www.structurepoint.com

---

## Proposal Request No. 007

**Project Name:** Loeb Stadium  
**Project Number:** 2015.02410  
**Date:** 02/03/2020

---

### OWNER:

City of Lafayette, Indiana – Board of Public Works and Safety  
20 North 6<sup>th</sup> Street  
Lafayette, IN 47901

### ARCHITECT / STRUCTURAL ENGINEER / CIVIL ENGINEER

American Structurepoint, Inc.  
9025 River Road, Suite 200  
Indianapolis, Indiana 46240  
317.547.5580

### MECHANICAL / PLUMBING / ELECTRICAL ENGINEER

Applied Engineering Services, Inc.  
5975 Castle Creek Parkway N Drive, Suite 300  
Indianapolis, IN 46250  
317.810.4141

---

This Proposal Request is for informational and pricing purposes only and shall not be interpreted as instruction to perform the proposed Work indicated herein. Contractor shall detail all costs associated with the Work, itemized at a minimum by labor, material, overhead and profit. Specify whether the change in Work is an ADD, DEDUCT or NO CHANGE to the contract. After receiving pricing, the Architect shall direct the Contractor regarding how to proceed. If, and only if, the Work outlined in this Proposal Request causes no change in Contract sum or time, the Contractor may then proceed with the Work listed herein, at which point, said Work shall become part of the Contract Documents and modify the original Contract Documents and all prior changes as applicable. Requirements of the original Contract Documents and previous changes remain in effect except as modified by this Proposal Request.

The extent of this Proposal Request is as follows:

### DOCUMENT MODIFICATIONS

#### PROJECT MANUAL

- A. No Change

#### DRAWINGS

- A. See clouded revisions on the attached drawings.
1. C302 – Grading Plan – Updated Grading for Terrace Area at Home Bullpen
  2. C402, C404, C405 – Utility Plan – Updated Drainage at Terrace near Home Bullpen, showing additional underdrains at bullpen and dugout areas.

END OF PROPOSAL REQUEST.









  
**J. R. KELLY COMPANY**  
GENERAL CONTRACTORS

March 2, 2020

Kettelhut Construction Inc.  
740 Sagamore Parkway South  
Lafayette, IN 47905

Attn: Alex Gonzalez

Re: PR #007 (Field Drainage Changes) Proposal  
Loeb Stadium – General Trades

J.R. Kelly Company is pleased to provide pricing associated with the changes shown in PR #007 (as described and noted on the attached documents). According to our previous discussions we are including the new underdrains at the batting cage and both bullpens along with the underground piping for the field terrace area. We have not included the actual drains for the field terrace area (during discussions the drains were assigned to DA Dodd). The cost associated with this work is:

R&W Contracting	\$5,159
JR Kelly 5% OH&P	\$258
Bond	\$54
<b>TOTAL LUMP COST FOR CHANGE ...</b>	<b>\$5,471</b>

Our proposal is valid for 30 days. Please issue a Change Order for this work if you would like for us to incorporate this change into our work. If you have any questions or need additional information please contact our office at your earliest convenience. Thank you for the opportunity to work with you on this project.

Sincerely,



Robert Mutzl P.E.  
Executive VP

Attachment: R&W Proposal and PR 7 with Notes

Request for Change - Loeb Stadium

To:  
 Rob Mutzl  
 JR Kelly Company

2/28/2020

From:  
 R&W Contracting, Inc.  
 3131 Klondike Road  
 West Lafayette, IN 47906  
 765-499-9390

**PR 07 - Batting Cage Underdrain / Field Terrace Drainage / Bull Pen Underdrains**

<u>Description</u>	<u>Rate</u>	<u>Quantity</u>		<u>Total</u>
Komatsu PC 78	75	8	HR	600
Takehuci TL 10	70	8	HR	560
Superintendent	70	8	HR	560
Operator	60	16	HR	960
Laborer	50	8	HR	400
8" HDPE N-12 Dual Wall	2.3	47	LF	108
4" HDPE N-12 Dual Wall	1.2	216	LF	259
18" Repair Coupler	32	2	EA	64
18"x4" HDPE Tee	125	2	EA	250
8"x4" HDPE Tee	67	3	EA	201
8" 90° HDPE Elbow	31	1	EA	31
8" 45° HDPE Elbow	31	1	EA	31
4" 45° HDPE Elbow	12	3	EA	36
#8 Stone (Delivered)	15.75	40	TN	630
Subtotal				\$ 4,690
P&OH (10%)				\$ 469
<b>Total</b>				<b>\$ 5,159</b>

R & W CONTRACTING INC  
3131 KLONDIKE ROAD  
WEST LAFAYETTE, IN

TEAM EJP Lafayette, IN.  
400 Hamman Street  
Lafayette, IN

47906

47905

Telephone: 765-449-2723

2/28/20 Bid ID: 5418163 LOEB DUAL WALL FITTINGS

Page 1

Quantity	Sell Per	Description	Unit Price	Extended Price
20	FT	8 ADS N12 PIPE SOIL-TITE	2.30	46.00
20	FT	4 ADS N12 PIPE SOIL-TITE	1.20	24.00
1	EA	18X4 ADS N12 TEE	125.00	125.00
1	EA	8X4 ADS N12 TEE WYE SOIL-TITE	67.00	67.00
1	EA	8" X 4" ADS N-12 TEE 8 ADS N12 90 ELBOW SOIL-TITE	31.00	31.00
1	EA	8" ADS N-12 BEND 90 8 ADS N12 45 BEND SOIL-TITE	31.00	31.00
1	EA	4 ADS N12 45 ELBOW SOIL-TITE	12.00	12.00
1	EA	4" ADS N-12 BEND 45 18 ADS SPLIT COUPLER	32.45	32.45

Subtotal: 368.45

Tax: .00

Bid Total: 368.45

**740 Sagamore Parkway South  
Lafayette, IN 47905  
(765) 447-2181  
Fax (765) 447-7122**

March 17, 2020

Mr. Dan McCloskey  
American Structurepoint, Inc.  
9025 River Road, Suite 200  
Indianapolis, IN 46240

Re: Loeb Stadium Renovation  
Lafayette, Indiana  
Kettelhut Project No. 6617

Gentlemen:


Enclosed please find cost documentation from applicable Contractors regarding Proposal Request No. 008, as it pertains to hardware changes. We have yet to receive responses from Contractors labeled N/R, but do not anticipate any other costs or credits than those shown below.

1.	BP #1 – General Trades	JR Kelly Co., Inc.	<\$ 2,788.00>
2.	BP #2 – Masonry	James Scherer Masonry, Inc.	N/R
3.	BP #3 – Steel	Almet, Inc.	N/R
4.	BP #4 – Roofing	Horning Roofing & Sheet Metal Co., LLC	N/R
5.	BP #5 – Alum.	Central Indiana Glass & Glazing, Inc.	<\$ 198.00>
6.	BP #6 – Fire Sprinklers	Dalmatian Fire, Division of Shambaugh & Son, L.P.	N/R
7.	BP #7 – Mechanical	D. A. Dodd, LLC	N/R
8.	BP #8 – Electrical	Huston Electric, Inc.	<\$ 1,049.00>
9.	BP #9 – Sports Lighting	Custer Electric, Inc.	N/R
10.	BP #10 – Scoreboard		
11.	BP #11 – Turf	Sprinturf, Inc.	N/R
12.	BP #12 – Stadium Seat	Irwin Seating Company	N/R
13.	BP #13 – Food Service	C&T Design & Equipment Co.	N/R
			<u>&lt;\$ 4,035.00&gt;</u>

After your review, if this cost data is approved by your firm and the Owner, please advise in order for a Change Order to be initiated.

Sincerely,

KETTELHUT CONSTRUCTION, INC.


  
D. Alex Gonzalez  
Executive Vice President

DAG: jas

Enclosure

cc: Field Office  
City of Lafayette w/enclosure  
Field Order 6617.042



  
**J.R. KELLY COMPANY**  
GENERAL CONTRACTORS

March 2, 2020

Kettelhut Construction Inc.  
740 Sagamore Parkway South  
Lafayette, IN 47905

Attn: Alex Gonzalez


Re: PR #008 (Door Hardware Changes) Proposal  
Loeb Stadium – General Trades

J.R. Kelly Company is pleased to provide pricing associated with the changes shown in PR #008 (as described and noted on the attached documents). According to your email clarification this morning the intent for the G001, G002 and G003 gates (that show electronic access hardware on the revised hardware specifications) is for the single Card Reader included for Gate 004 to operate all four gates simultaneously. Please also note that the changes to the hardware for doors 010B, 011B, 012A and 018A were all provided and accepted under PR 005 and thus are not included in this pricing. As a last note, all electrical wiring for the card readers and access system are to be included in the electrical contractor's scope. Thus Huston Electric should be providing pricing for any electrical work associated with the changes and is not included in our pricing. The cost associated with the work described in the PR is:

Mulhaupts	(\$2,760)
Bond	<u>(\$28)</u>
<b>TOTAL LUMP DEDUCT FOR CHANGE ...</b>	<b>\$2,788</b>

Our proposal is valid for 30 days. Please issue a Change Order for this work if you would like for us to incorporate this change into our work. If you have any questions or need additional information please contact our office at your earliest convenience. Thank you for the opportunity to work with you on this project.

Sincerely,



Robert Mutzl P.E.  
Executive VP

Attachment: Mulhaupt's Proposal

8227 Northwest Blvd. #270  
Indianapolis, IN 46278



209 North 5<sup>th</sup> Street  
Lafayette, IN 47901

Phone: (317) 228-9470  
Fax: (317) 228-9479

Phone: (765) 423-2610  
Fax: (765) 423-2622

FOUNDED 1876

**"Today's Innovators for Tomorrow's Solutions"**

**Date:** February 13, 2020  
**To:** J.R. Kelly Company Inc  
**Attention:** Rob Mutzl  
**Project:** 19114 Loeb Stadium  
**Reference:** Change Order -- PR# 008  
**Quoted by:** Richard Woodhead -- 765-807-5908 -- richardw@mulhaupt.com

The following changes may result in an add or deduct to the contract amount of this project. These prices do not include sales tax unless listed separately below and are F.O.B. jobsite. Pricing valid for 60 days. Price excludes installation, glass & glazing. No material will be ordered until a signed copy of this change request is received by this office.

Changes included in this price quotation:

- 1) Change doors 002 and 004 to passage set vs. card access.  
**DEDUCT: <\$1,140.00>**
- 2) Doors 010B and 011B change to push pulls.  
**DEDUCT GIVEN AND TAKEN UNDER PR# 5**
- 3) Change doors 002A and 113 to keyed lockset vs. card access.  
**DEDUCT: <\$1,080.00>**
- 4) Change doors 012A and 018A to keyed lockset vs. card access.  
**DEDUCT GIVEN AND TAKEN UNDER PR# 5**
- 5) Deduct at opening 201B and 213B to card reader only.  
**DEDUCT: <\$216.00>**
- 6) Deduct at openings G001, G002, and G003 to card reader only.  
**DEDUCT: <\$324.00>**

**TOTAL = (\$2,760)** →

*By signing below and returning this change request, you authorize Mulhaupt's, Inc. to proceed on the above work and agree to the price set above. Note that this will change your contract value accordingly. Please forward your formal change order.*

Authorized by: \_\_\_\_\_ Title: \_\_\_\_\_ Date: \_\_\_\_\_  
*Signature*

**740 Sagamore Parkway South  
Lafayette, IN 47905  
(765) 447-2181  
Fax (765) 447-7122**

March 2, 2020

Mr. Dan McCloskey  
American Structurepoint, Inc.  
9025 River Road, Suite 200  
Indianapolis, IN 46240

Re: Loeb Stadium Renovation  
Lafayette, Indiana  
Kettelhut Project No. 6617

Revision #1

Gentlemen:


Enclosed please find cost documentation from applicable Contractors regarding changes to the foul poles as indicated in the response to RFI #70. We have yet to receive responses from Contractors labeled N/R, but do not anticipate any other costs or credits than those shown below.

1. BP #1 – General Trades	JR Kelly Co., Inc.	\$ 987.00
2. BP #2 – Masonry	James Scharer Masonry, Inc.	N/R
3. BP #3 – Steel	Almet, Inc.	N/R
4. BP #4 – Roofing	Horning Roofing & Sheet Metal Co., LLC	N/R
5. BP #5 – Alum.	Central Indiana Glass & Glazing, Inc.	N/R
6. BP #6 – Fire Sprinklers	Dalmatian Fire, Division of Shambaugh & Son, L.P.	N/R
7. BP #7 – Mechanical	D. A. Dodd, LLC	N/R
8. BP #8 – Electrical	Huston Electric, Inc.	N/R
9. BP #9 – Sports Lighting	Custer Electric, Inc.	N/R
10. BP #10 – Scoreboard		
11. BP #11 – Turf	Sprinturf, Inc.	N/R
12. BP #12 – Stadium Seat	Irwin Seating Company	N/R
13. BP #13 – Food Service	C&T Design & Equipment Co.	N/R
		<u>\$ 987.00</u>

After your review, if this cost data is approved by your firm and the Owner, please advise in order for a Change Order to be initiated.

Sincerely,

KETTELHUT CONSTRUCTION, INC.



D. Alex Gonzalez  
Executive Vice President

DAG: jas

Enclosure

cc: Field Office  
City of Lafayette w/enclosure  
Field Order 6617.045





**J. R. KELLY COMPANY**  
GENERAL CONTRACTORS

February 24, 2020

Kettelhut Construction Inc.  
740 Sagamore Parkway South  
Lafayette, IN 47905

Attn: Alex Gonzalez


Re: RFI 70 Foul Pole Changes Proposal - REVISED  
Loeb Stadium – General Trades

J.R. Kelly Company is pleased to provide pricing associated with the changes to the foul poles as shown in the answers to RFI #70. The RFI response changed the left field foul pole to being mounted on top of the outfield wall and the right field pole to being mounted to the side of one of the pilasters on top of the outfield wall. These changes require the addition of a pilaster to the left field wall per American Structurepoint detail SSK-001 (ASK-003) and required Sportsfield Specialties to provide custom foul poles. The cost associated with this work is:

Sportsfield Specialties	\$1,135	
Anchor Bolt -Install	\$64	
Add'l Rebar -Material	\$110	
-Install	\$55	
Pilaster Forming - Material	\$160	
-Labor	\$499	
Subtotal	\$2,023	\$888
10% OH&P	\$202	\$89
Bond	\$22	\$10
<b>TOTAL LUMP COST FOR CHANGE ...</b>	<b><del>\$2,247</del></b>	<b>\$987</b>

Our proposal is valid for 30 days. Please issue a Change Order for this work if you would like for us to incorporate this change into our work. If you have any questions or need additional information please contact our office at your earliest convenience. Thank you for the opportunity to work with you on this project.

Sincerely,



Robert Mutzl P.E.  
Executive VP

Attachment: Back-up Proposals



Carter-Water South Bend, IN  
 910 W. Ireland Road  
 South Bend, IN 46614  
 (574) 231-9000

# Rebar Quote

**Project Name:** Loeb Stadium - Extra Wall Pilaster  
**Project Location:** Lafayette, IN  
**Pages Used For Estimate:** SSK-001  
**Drawings Dated:** 1/22/2020  
**Addendums:**

**Quote Date:** 2/11/2020  
**Bid Date:** 2/11/2020  
**Quote #:** 20-061

Any additional waivers of subrogation or additional insured status may result in additional fees/costs not included on this quote. If a supply bond is requested, the cost will be billed to the contractor. Sales tax is NOT included in this quote. Freight charges may apply. Terms are NET 30.

This Quotation will expire **30 days** from Quote Date.

**Base Bid:**

<u>Building Foundations:</u>	<u>Quantity</u>	<u>Unit</u>	<u>Ext. Price</u>
Includes -		Tons	

**Total Net Price:**

<u>Masonry:</u>	<u>Quantity</u>	<u>Unit</u>	<u>Ext. Price</u>
Includes -	N/A	Tons	

**Total Net Price:**


<u>Site Work:</u>	<u>Quantity</u>	<u>Unit</u>	<u>Ext. Price</u>
Includes -	200	Pounds	\$ 110.00
		Pier Verticals & Pier Ties	


**Total Net Price:** \$ 110.00

All rebar quoted above to be delivered in 1 truckload.  
 Any additional loads may be subject to a minimum of \$100.00 shipping charge.




# FOUL POLE BASE PILASTER

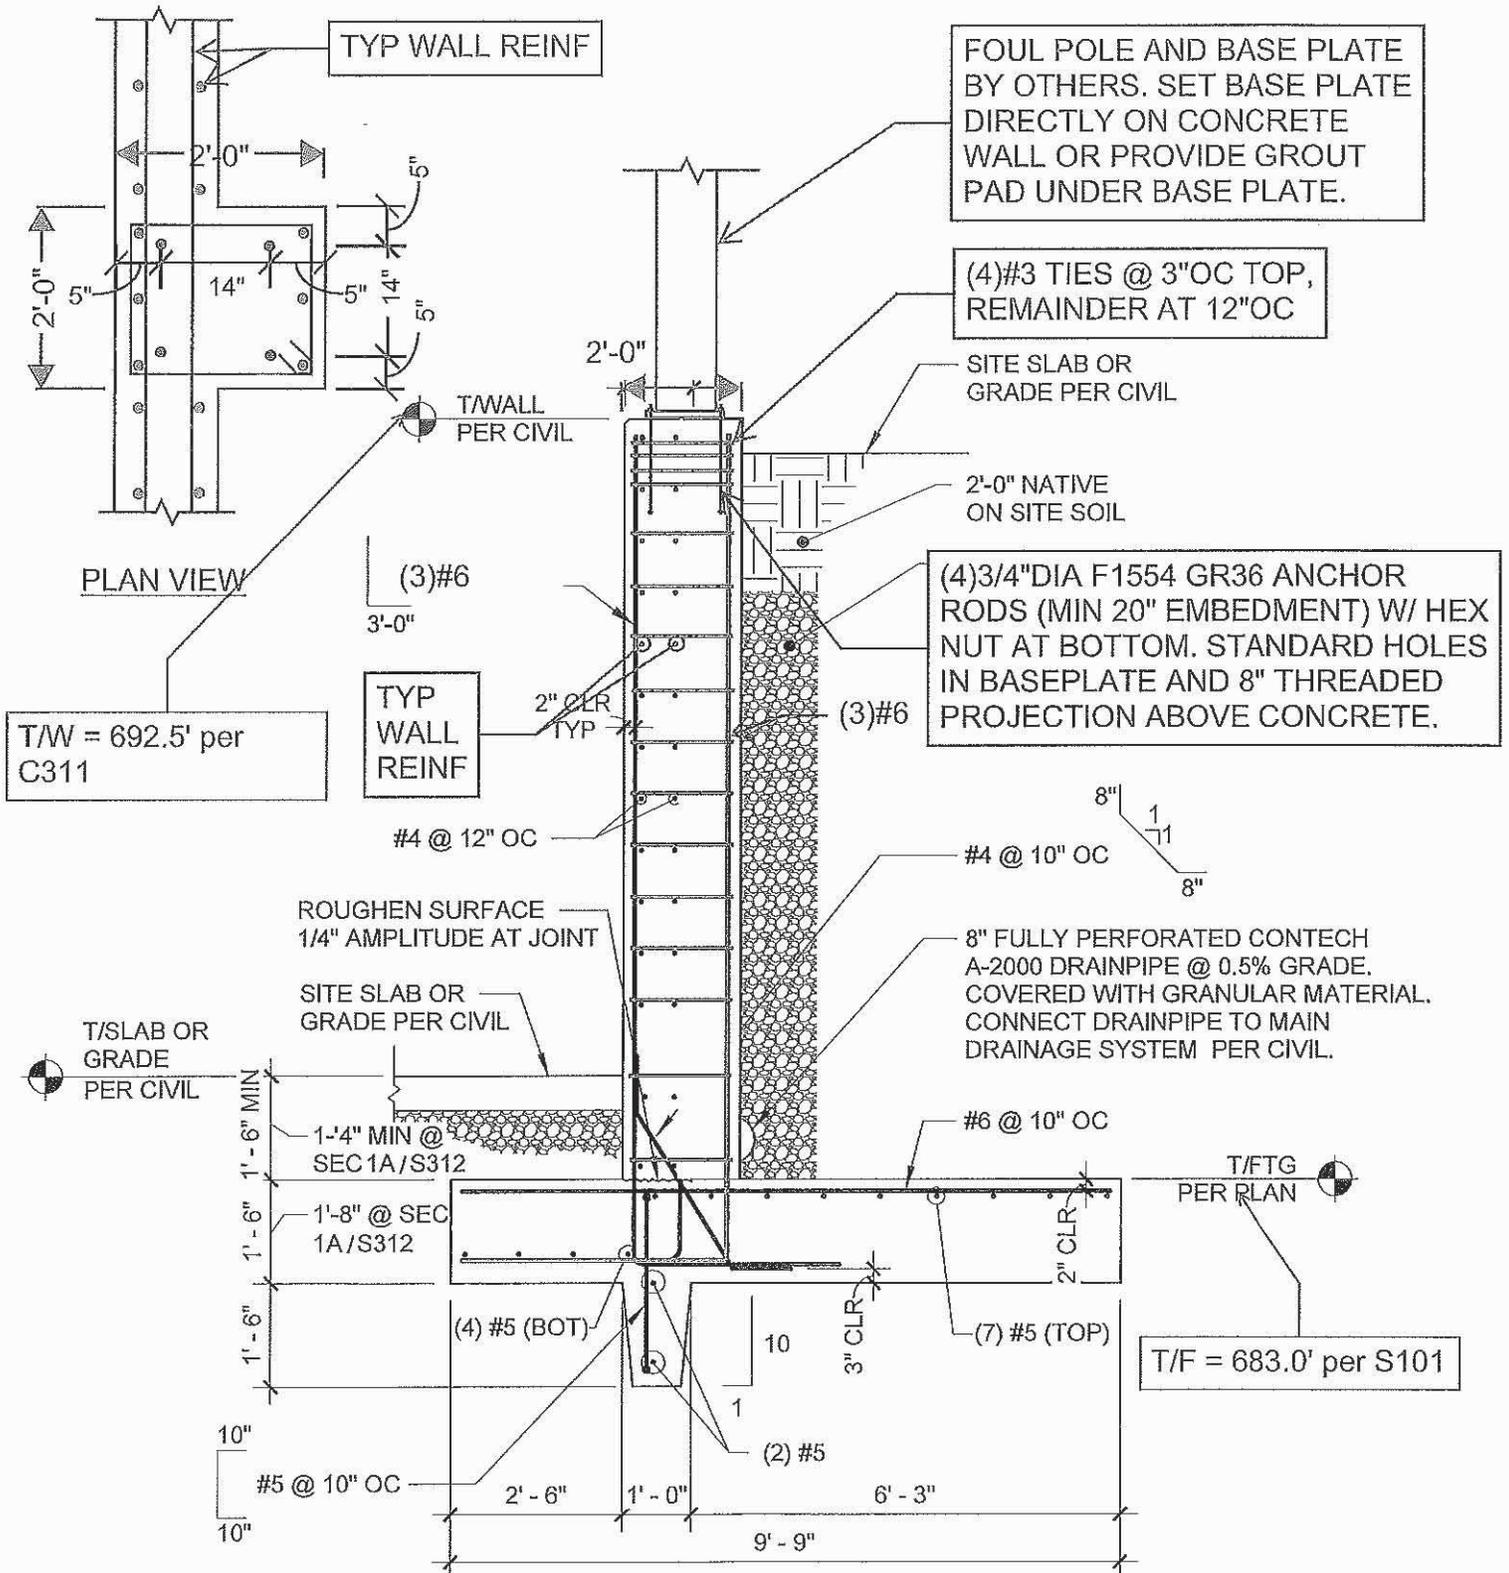

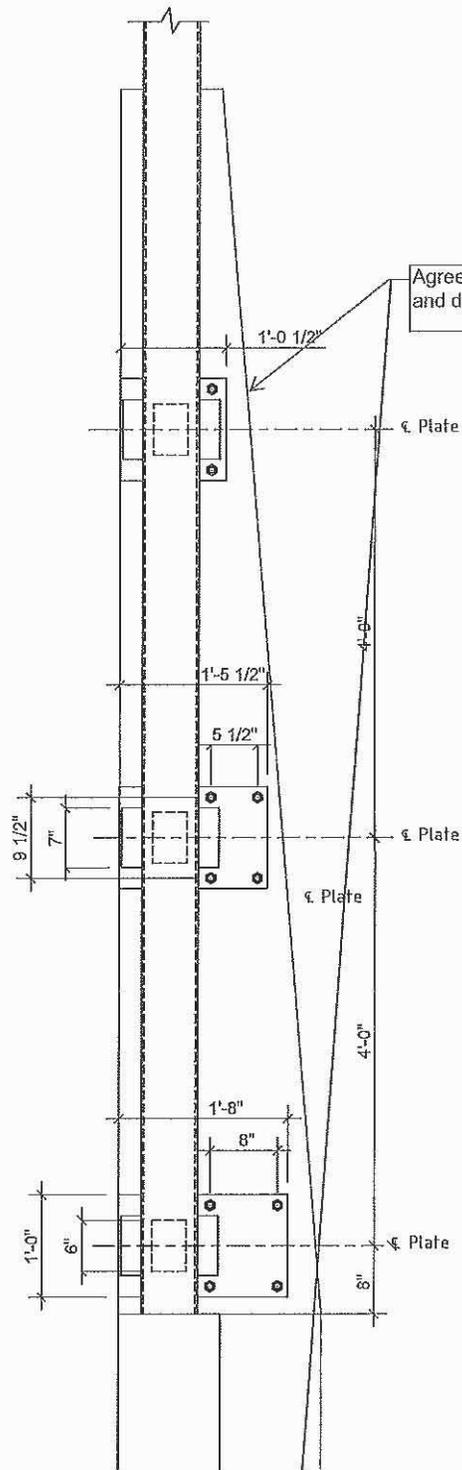

Agreed upon custom mounting for pole and dimensions from wall pilaster



Approved by the Board of Public Works and Safety on the \_\_\_\_\_ day of  
\_\_\_\_\_, 2020.

\_\_\_\_\_  
Gary Henriott, President

\_\_\_\_\_  
Cindy Murray, member

\_\_\_\_\_  
Norm Childress, member

\_\_\_\_\_  
Ronald Shriner, member

\_\_\_\_\_  
Amy Moulton, member

ATTEST:

\_\_\_\_\_  
Mindy Miller, Deputy Clerk

Date: \_\_\_\_\_
